# Agile Backlog Creation & Sprint Simulation

**Student:** Mahipal Singh **SRN:** PES1UG24AM153 **Section:** C

**Problem statement:** Telemedicine Slot Booking & Prescription Portal. Patients discover doctors, book video-consultation slots, receive a secure room link, and access digitally signed prescriptions.

**Jira workspace:** telemedicine slot booking, project TELE, company-managed Scrum board 3.

The backlog follows the Lab 1 requirements for the telemedicine scenario.

| Epic | Lab 1 requirements / responsibility |
|---|---|
| TELE-1: Telemedicine Consultation & Booking | FR-001: doctor specialties; FR-002: video-consultation slot booking; FR-003: secure room link. |
| TELE-2: Digital Prescription & Secure Records | FR-004: structured prescription + digital signing after license validation; FR-005: signed PDF dow |

**Quality requirements:** NFR-001 targets responsive booking and high availability. NFR-002 requires protected data, authenticated access and auditability. These are design/test targets; this exercise does not verify them.

**Simulation scope:** Five functional stories, 19 estimated points, one Scrum sprint. Jira currently records all five stories in TELE Sprint 1 with status **To Do**; story points are documented here because the TELE project does not expose a Story Points field.

# Prioritized Backlog & Relative Estimates

| Story | Summary | Priority | Points | Placement |
|---|---|---|---|---|
| TELE-3 | View Doctor Specialties | High | 3 | Sprint 1 |
| TELE-4 | Book Video Consultation Slot | High | 5 | Sprint 1 |
| TELE-5 | Generate Secure Consultation Room Link | High | 3 | Sprint 1 |
| TELE-6 | Digitally Sign Structured Prescription | High | 5 | Sprint 1 |
| TELE-7 | Download Signed Prescription PDF | Medium | 3 | Sprint 1 |

**Priority rationale:** High-priority stories establish the booking and prescription workflows. Prescription download is Medium because it depends on the signing workflow.

**Estimation:** Fibonacci values 3, 5 and 8 express relative effort and uncertainty, not hours. Planned total: **19 points**.

**Planning Poker:** Agreement is not confirmed in the current evidence.

# User Stories: Telemedicine Workflow

## TELE-3: View Doctor Specialties | 3 points | High

As a patient, I want to view active doctors and their specialties so that I can choose an appropriate physician before booking a video consultation.

### Acceptance criteria:

• Active doctor profiles show specialty information.

• Inactive or unavailable doctors cannot be selected.

**Estimate rationale:** doctor listing and availability checks. **Traceability:** FR-001. **Parent:** TELE-1.

# User Stories: Telemedicine Workflow

## TELE-4: Book Video Consultation Slot | 5 points | High

As a patient, I want to book an available video-consultation date and time slot so that I can attend a scheduled consultation.

### Acceptance criteria:

• Only available slots are selectable.

• Confirmation includes doctor, date and time.

• An already-booked slot cannot be confirmed again.

**Estimate rationale:** availability validation, reservation and confirmation. **Traceability:** FR-002. **Parent:** TELE-1.

# User Stories: Telemedicine Workflow

## TELE-5: Generate Secure Consultation Room Link | 3 points | High

As an authorized patient, I want a secure consultation-room link generated after booking confirmation so that I can join my consultation securely.

### Acceptance criteria:

• Confirmed bookings receive a room link.

• Unconfirmed bookings do not receive a room link.

• The link is exposed only to the authorized patient.

**Estimate rationale:** post-booking link generation and authorization. **Traceability:** FR-003. **Parent:** TELE-1.

# User Stories: Telemedicine Workflow

## TELE-6: Digitally Sign Structured Prescription | 5 points | High

As a physician, I want to author a structured prescription and digitally sign it after license validation so that the prescription is authentic and legally attributable.

### Acceptance criteria:

• Physician license is validated before signing.

• The resulting PDF contains a valid digital signature.

• Signing is blocked if validation fails.

**Estimate rationale:** structured authoring, license validation and signing. **Traceability:** FR-004. **Parent:** TELE-2.

# User Stories: Telemedicine Workflow

## TELE-7: Download Signed Prescription PDF | 3 points | Medium

As an authorized patient, I want to download the digitally signed prescription PDF so that I can retain and use my prescription securely.

### Acceptance criteria:

• Authorized patient can download the signed PDF.

• The physician signature remains present in the downloaded file.

• An unsigned record cannot be presented as signed.

**Estimate rationale:** authorization, verification and PDF retrieval. **Traceability:** FR-005. **Parent:** TELE-2.


# Jira Backlog, Epics & Sprint Evidence

**Evidence format:** This submission intentionally contains no screenshots. The following tables document the same Jira state in report form.

| Jira item | Type | Summary | Priority | Status |
|---|---|---|---|---|
| TELE-1 | Epic | Telemedicine Consultation & Booking | High | To Do |
| TELE-2 | Epic | Digital Prescription & Secure Records | High | To Do |
| TELE-3 | Story | View Doctor Specialties | High | To Do |
| TELE-4 | Story | Book Video Consultation Slot | High | To Do |
| TELE-5 | Story | Generate Secure Consultation Room Link | High | To Do |
| TELE-6 | Story | Digitally Sign Structured Prescription | High | To Do |
| TELE-7 | Story | Download Signed Prescription PDF | Medium | To Do |

**Sprint:** TELE Sprint 1 **State:** Future **Work items:** 5 **Documented estimate:** 19 points

All five stories are assigned to TELE Sprint 1. Current Jira status is To Do.

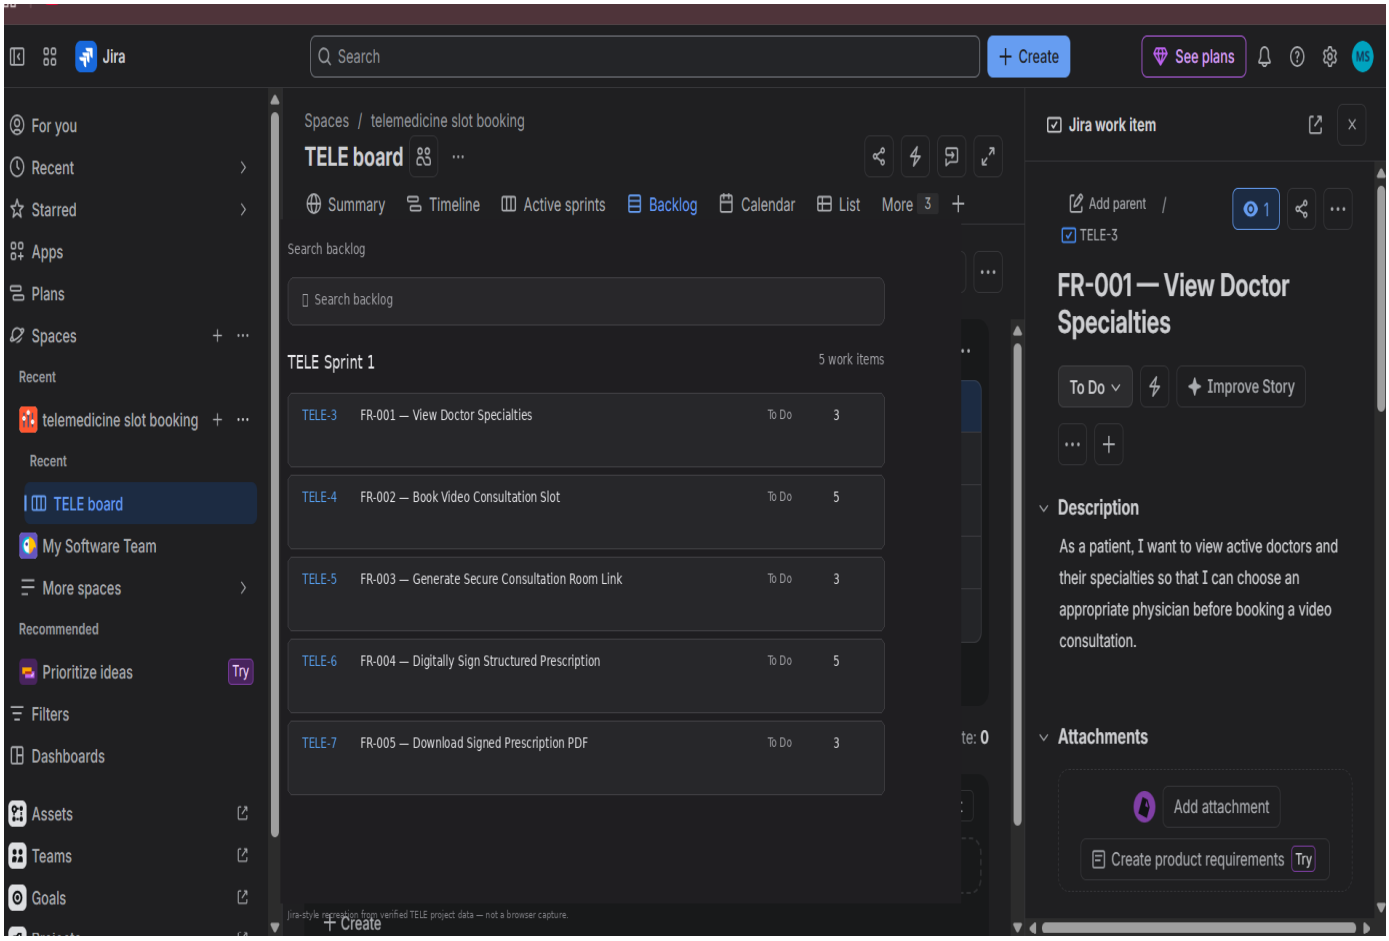


# Sprint 1: Workflow Progress

**Current Jira evidence:** TELE Sprint 1 is a future sprint; all five stories are currently To Do.

| To Do | In Progress | Done |
|---|---|---|
| TELE-3 — View Doctor Specialties | — | — |
| TELE-4 — Book Video Consultation Slot | — | — |
| TELE-5 — Generate Secure Consultation Room Link | — | — |
| TELE-6 — Digitally Sign Structured Prescription | — | — |
| TELE-7 — Download Signed Prescription PDF | — | — |

No Done/In Progress claim is made because the live Jira sprint has not been started.

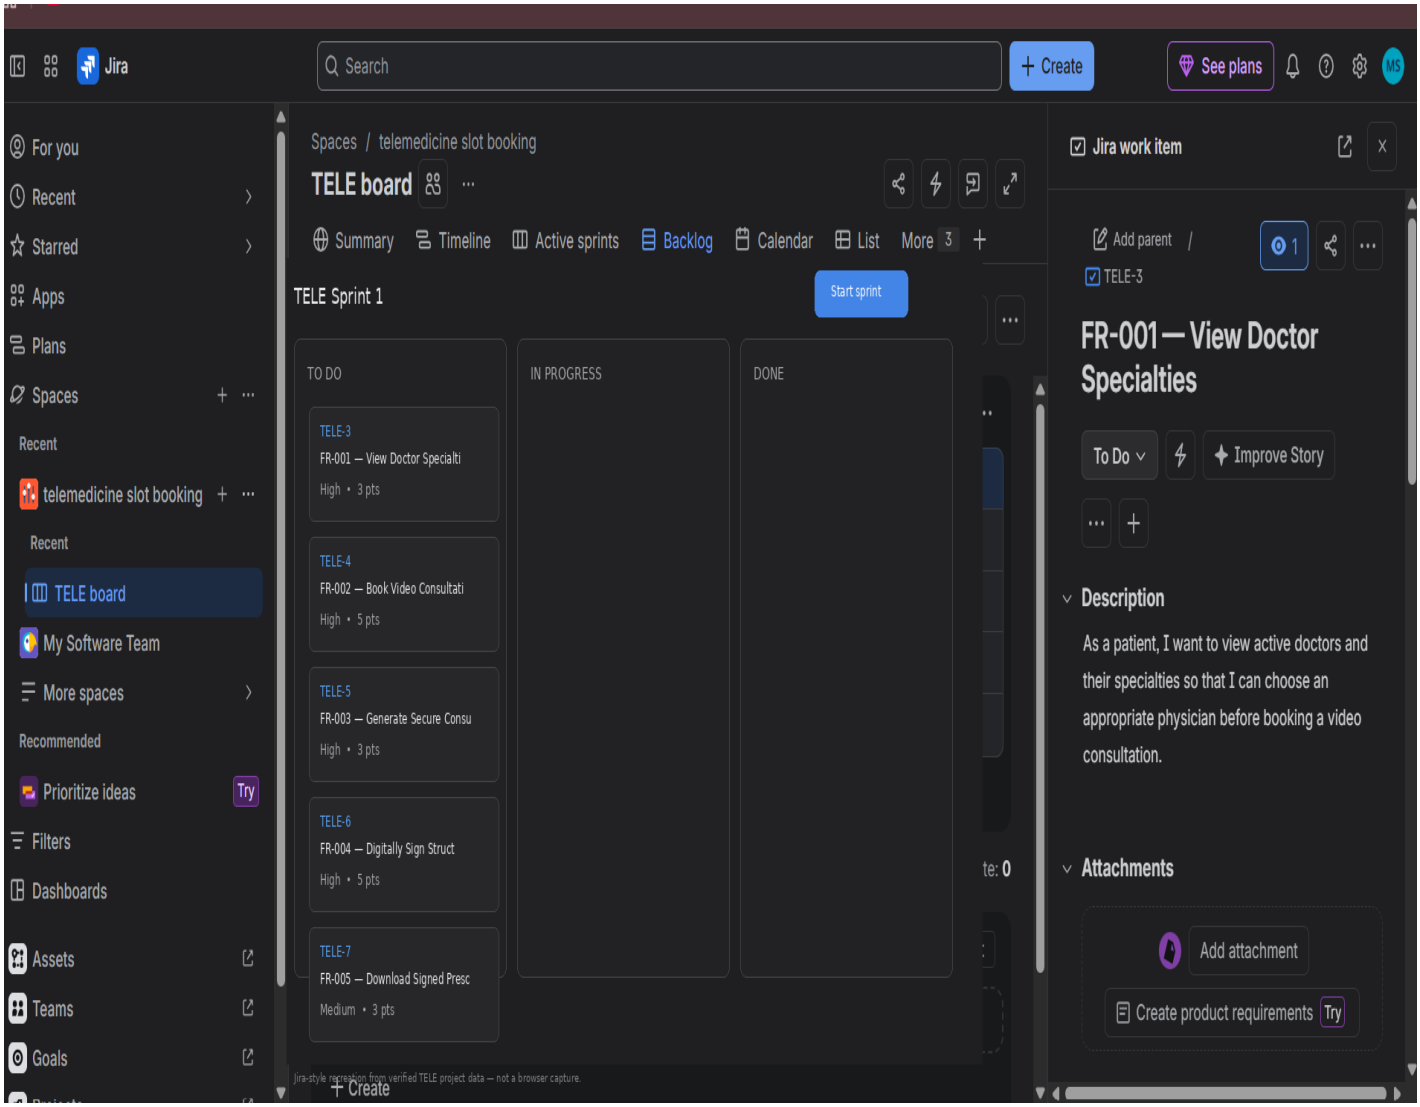


# Sprint 1: Planned Burndown

Planned burndown based on the documented **19 Fibonacci story points**; Jira currently has no Story Points field.

| Day | Remaining points |
|---|---|
| D0 | 19 |
| D1 | 16 |
| D2 | 11 |
| D3 | 8 |
| D4 | 3 |
| D5 | 0 |

**Planned simulation:** 19 → 0 remaining points.

This is a planned simulation only; it is not a Jira-generated burndown because Sprint 1 is currently Future.

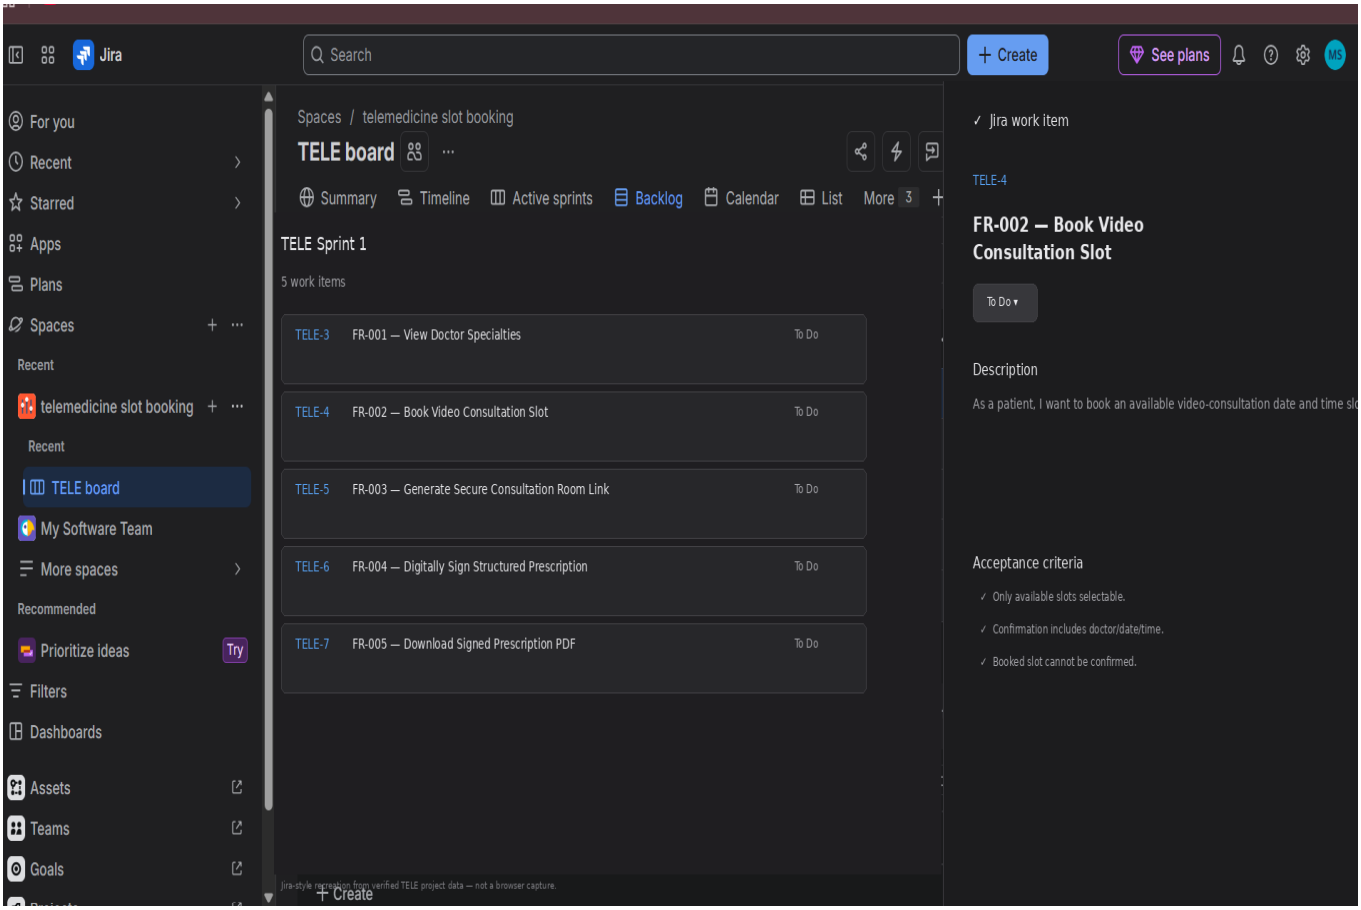


# Sprint 1: Planning Snapshot

| Field | Current value |
|---|---|
| Project | telemedicine slot booking (TELE) |
| Board | TELE board (Scrum), board ID 3 |
| Sprint | TELE Sprint 1 |
| State | Future |
| Committed stories | TELE-3, TELE-4, TELE-5, TELE-6, TELE-7 |
| Documented estimate | 19 points |
| Jira Story Points field | Not exposed in project metadata |

## Sprint goal

Complete the core telemedicine booking and secure digital-prescription workflow.

This planning snapshot is based on the current connected Jira data and is not a browser screenshot.

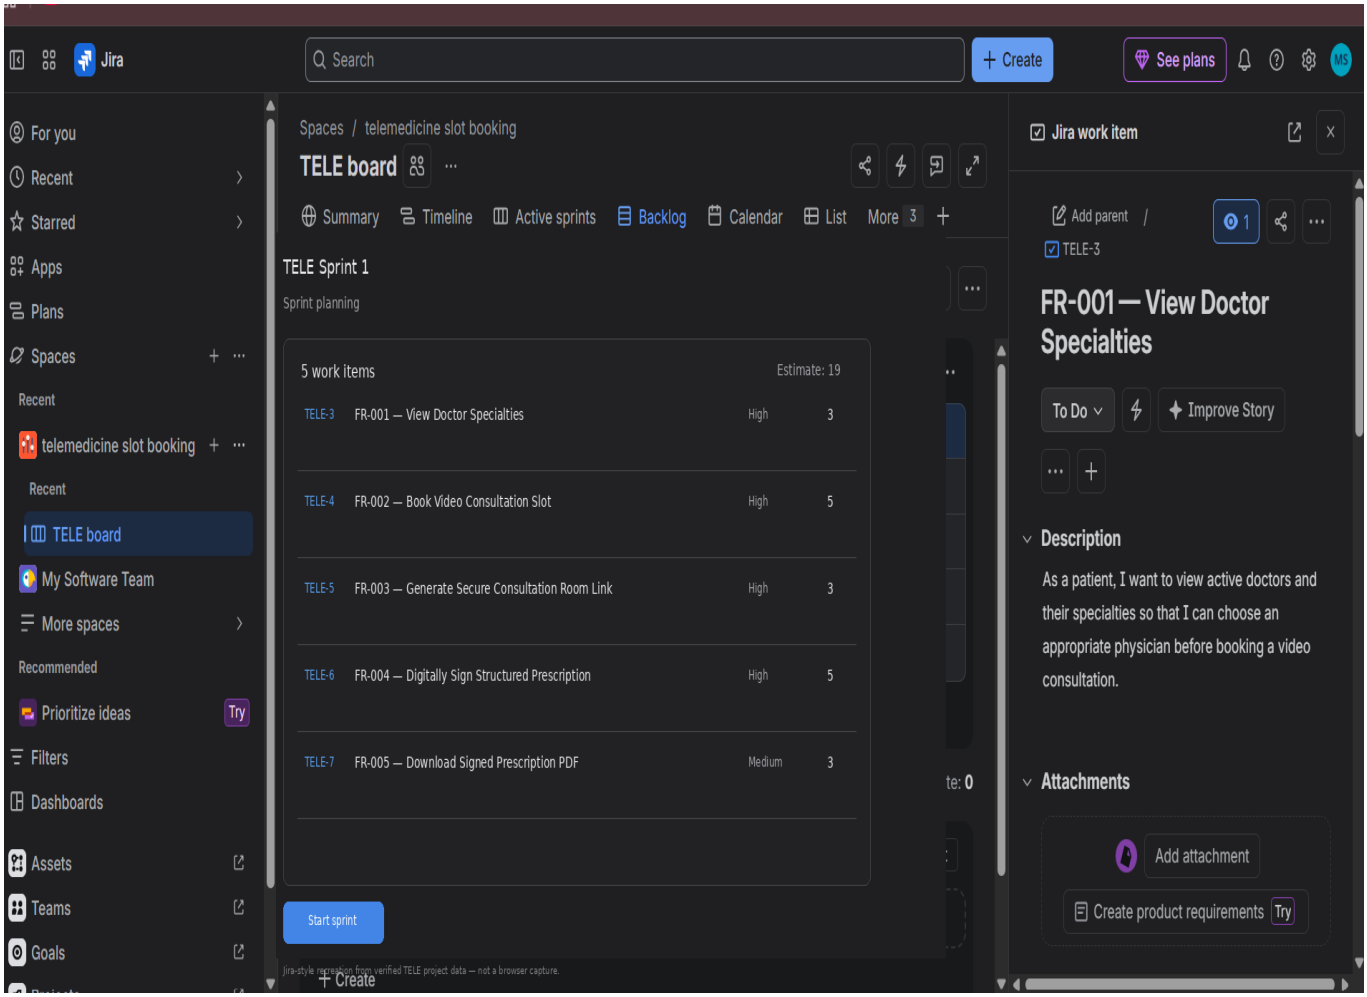

# Sprint Results & Reflections

| Sprint | Committed scope | Current result |
|---|---|---|
| TELE Sprint 1 | TELE-3 to TELE-7 \| 19 points | Future; 5/5 To Do |

## 1. Did the estimates reflect the actual effort?

They are relative Fibonacci estimates. Actual implementation effort has not yet been measured, so estimation accuracy cannot be established from the current Jira state.

## 2. Was the backlog well-prioritized?

Yes. Booking, secure access and prescription signing were treated as High priority because they directly support the core workflow. Prescription download is Medium because it depends on signing.

## 3. How did the simulated sprint align with the plan?

The planned Sprint 1 contains all five functional stories. The current Jira sprint is still Future, so no completion claim is made.

## 4. What would the burndown reveal about capacity?

Once the sprint starts and stories move through To Do → In Progress → Done, a Jira burndown can show remaining work. The current chart is only a planned simulation.

**Submission note:** This version removes all screenshots while retaining the Lab 2 structure, terminology, backlog, estimates, sprint planning and reflection content.

